

WEEKLY SUMMARY

# EAU CLAIRE SCHOOLS SOUTH MIDDLE SCHOOL

## SCHEDULE UPDATE

### Current Week:

- Market & Johnson continued with supervision and coordination. M&J poured concrete floor slab in front entrance addition. Continued interior stud framing. Masons finished exterior brick on area A addition. Started brick on area B addition.
- RTS roofing finished roofing front entrance addition.
- Winona Controls contained plumbing rough-in on area B science labs.
- Master Metals started installing ductwork in area B addition.
- B&B electric started electrical rough-in on area B addition.

### Upcoming Week:

- Market & Johnson will continue with supervision and coordination. Continue interior steel stud framing. Masons will continue exterior brick on area B addition.
- Winona Controls will continue plumbing rough-in.
- Master Metals will continue installing ductwork
- B&B electric will continue electrical rough-in.

## WEEKLY PHOTOS




framing walls in science room addition



Brick area A



Framing classroom walls area B 2<sup>nd</sup> floor

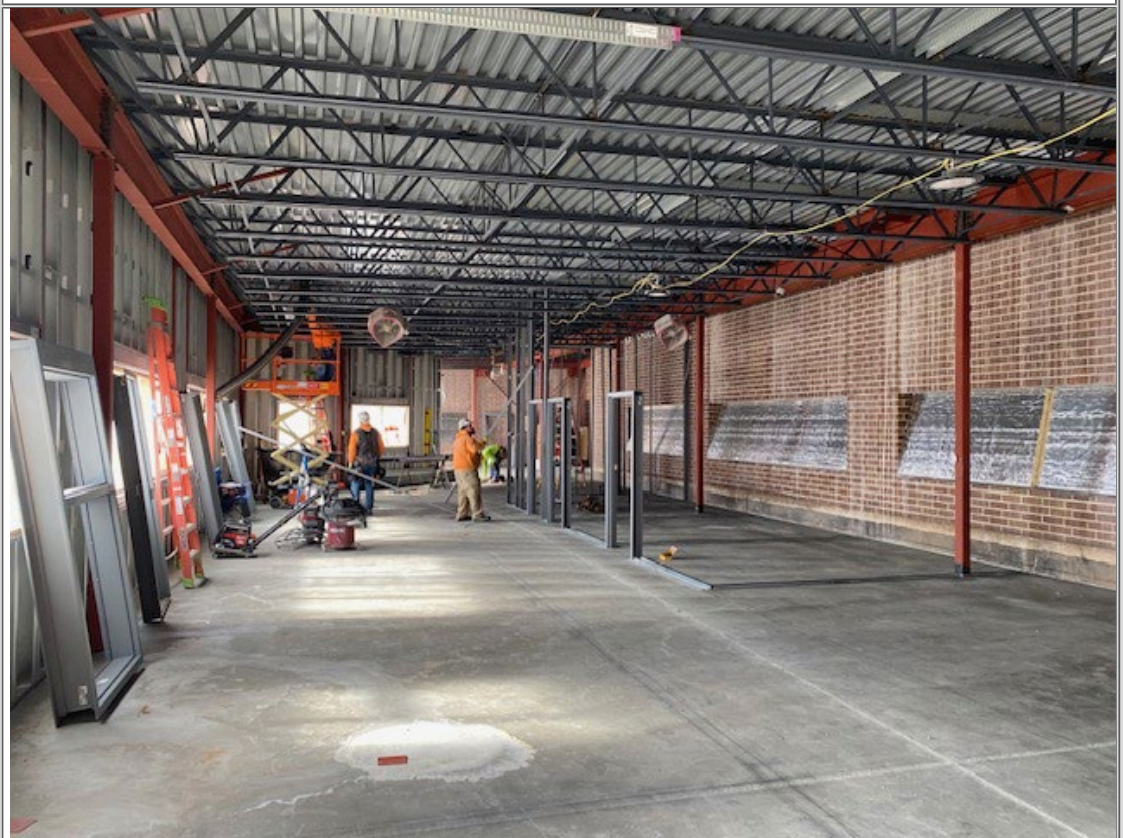

Floors poured at front entrance, started framing walls
