

REFERENDUM PROJECT UPDATES

DATE: July 19, 2024

NORTH PHASE 1 CLASSROOM/COMMONS ADDITION

The new classrooms are completed, and furniture has been placed into the rooms. They are beginning painting the commons and the teacher lounge. The project is still on schedule to finish before school begins.



3299-ECASD_North_H
S_Phase_1-21-2024-07

NORTH TURF PROJECT

The grading of the field will continue the week of the 19th, it will be reviewed towards the end of the week to verify that measurements are accurate. The light poles have been installed and final connections will happen when the bleachers are installed.



3358-ECASD_North_H
S_Turf_Field-7-2024-07

NORTH FLOORING REPLACEMENT

The carpeting is nearly completed in all classrooms that were being replaced. They have delayed the LVT installation until first week in August because of a scheduling conflict.




NORTH PHASE II ADDITION

Bidding is complete. A construction timeline will be developed after the board meeting on July 22.

NORTH BLEACHER REPLACEMENT

The old bleachers are completely removed, and the new electrical wiring is in place for the new bleacher system. The delivery of the framing and mechanical system for the new bleacher system is on site. The seats are estimated to arrive the week of the 22. They will begin installation Monday the 22.

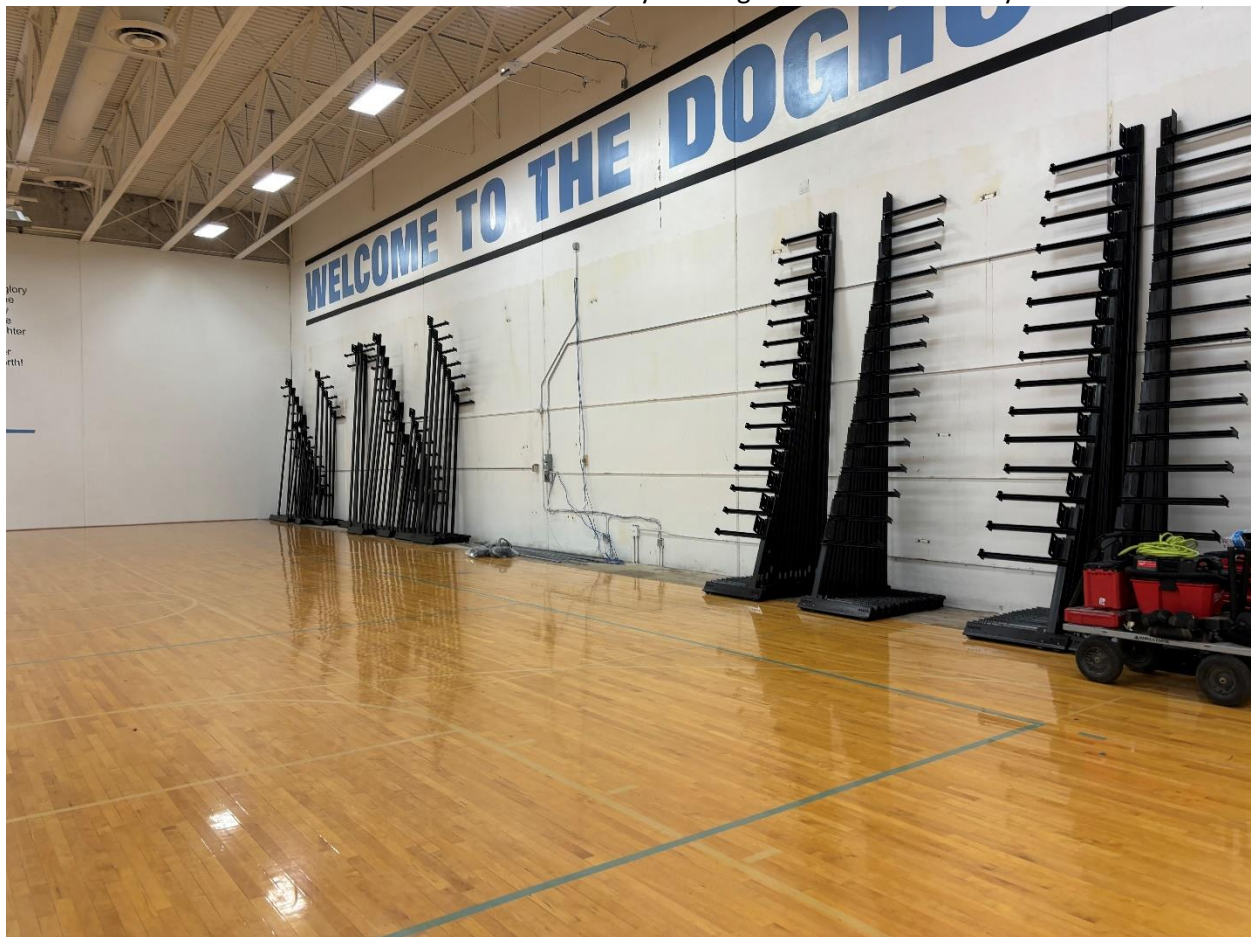



MEMORIAL PARKING LOT

Complete

MEMORIAL ROOF REPLACEMENT

They have begun removing and replacing the roof above the auditorium and the auditorium entrance. The weather has caused some delays, but they are working weekends and later during the evening to make up that missed time.



MEMORIAL FLOORING REPLACEMENT

The Project is complete.

NORTHWOODS CONCRETE REPLACEMENT

Complete

MEMORIAL TURF PROJECT

The light poles have been installed, and final hookup for power will be done when the bleachers are installed. They have begun running the new electrical service and will install the panels in the concession stand in the next few weeks. The installation of the turf has begun and they anticipate being completed in the next few weeks.



3357-ECASD_Memorial_HS_Turf_Field-7-202

LOCUST LANE, NORTHSTAR, NORTHWOODS, MEADOWVIEW HVAC REPLACEMENT

There have been no further delays, and the projects are moving within the allotted schedule.



3295-ECASD_HVAC_Equipment_Replacement

PUTNAM FLOORING REPLACEMENT

Complete

SOUTH CLASSROOM REMODELING

The 8th grade area has furniture being installed the week of 7/22. The main office has district supplied cabinetry being installed the week of 7/22. The FACS are and science area will have the cabinetry and painting being completed in the next few weeks. They will cut the opening for the 6th grade house windows later this week and install the windows the following week. The front parking lot will be resurfaced the week of 7/22.

