

REFERENDUM PROJECT UPDATES

DATE: July 1, 2024

NORTH PHASE 1 CLASSROOM/COMMONS ADDITION

Demolition is complete and they have begun building back the space. The rough in for the bathrooms has begun and should be completed in the next few days. The project is progressing on schedule.



3299-ECASD_North_H
S_Phase_1-18-2024-06

NORTH TURF PROJECT


They have completed the initial grading and outline of the field. The contractor will begin laying out the under-field drainage and continue to do the final grading before turf installation.



3358-ECASD_North_H
S_Turf_Field-4-2024-06

NORTH FLOORING REPLACEMENT

Demolition is completed in the rooms receiving new carpet and LVT tiles. The rooms receiving LVT tiles have all the prep work complete. The LVT will be installed the middle of July and the remaining carpeted rooms will be done the second week in July.

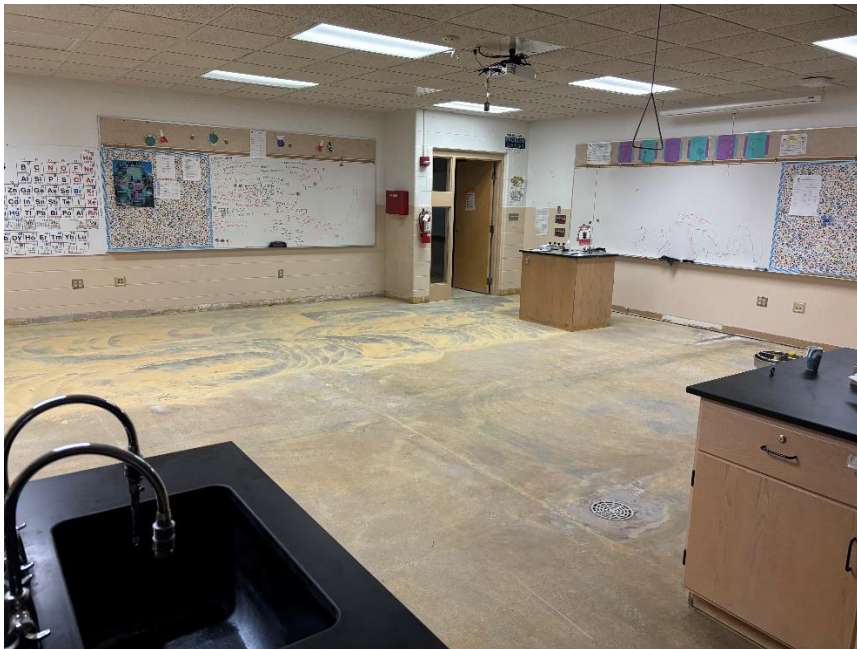

NORTH PHASE II ADDITION

Bidding is complete. A construction timeline will be developed after the board meeting on July 22.

NORTH BLEACHER REPLACEMENT

The bleacher demolition has begun and will be completed the second week in July. The installation of the new bleacher system will begin towards the end of July.

MEMORIAL ROOF REPLACEMENT

The demolition for the roof will begin later this week. They will mobilize this week and begin receiving materials for the project. The contractor will begin moving product onto the roof the week of July 1.

MEMORIAL FLOORING REPLACEMENT

They have completed demolition and reinstallation of the new flooring. The vinyl base has been delayed until the second week in July, at that time they will complete the punch list.



MEMORIAL PARKING LOT REPLACEMENT

They have finished the second lift on the majority of the parking lot. They have one area left to pave and will begin lining the lot later this week weather permitting.



MEMORIAL TURF PROJECT

Grading for the new turf field is nearly complete. They have installed the drainage system to help with removing the water from all the rain that has occurred in the last few days. They anticipate installing turf the week of July 8th.



3357-ECASD_Memorial_HS_Turf_Field-4-202

LOCUST LANE, NORTHSTAR, NORTHWOODS, MEADOWVIEW HVAC REPLACEMENT

Demolition complete, and they anticipate begin to reinstall equipment in the next few weeks.



3295-ECASD_HVAC_Equipment_Replacement

PUTNAM CLASSROOM ADDITION

The fire alarm and controls will be finished in the next few weeks. The construction and the punch lists have been completed. Relining of the parking lot is complete. We have put together the new furniture and placed it into the classrooms. We are waiting on IT to provide a part to finalize the installing the new TVs in each classroom.

PUTNAM FLOORING REPLACEMENT

The contractor has completed installation of the LVY in the hallways and most of the rooms. They will finish installation the week of July 1st and will install the base at that time. The carpet will be installed in the classrooms the second week in July.

SOUTH CLASSROOM REMODELING

The construction project is on schedule. They have completed the painting in the 8th grade house and will finalize above ceiling work the week of July 1st. The walls are being drywalled in the science area and should be completed in the next week. Demolition is complete in the 6th grade area; we will not begin any finish work until late August or early September. The main entrance and principals' office spaces are complete. We will begin installing cabinetry and furniture beginning the week of July 1st. Demolition on the remaining office space will be ongoing through the summer with finish work beginning late August. Concrete work should be completed the week of July 1st for the main entrance and additional sidewalks.



3302-South_Middle_S
chool_Additions_and_
