



WEEKLY PROJECT UPDATE

Current Week

- Market & Johnson continued supervising and coordinating trades. M&J continued installing TV brackets, door hardware, and corner guards in science. M&J begin installing drywall in Area D.
 - Overhead Door continued the fire shutter install.
 - Cleaners finished in the FCS Lab and Area A offices
 - The District finished setting appliances in the FCS Lab and continued with furniture throughout.
 - The Gym was cleaned out of construction material.
- B&B Electric, Master Metals, and Winona Controls continued installing devices and finishes in the science pod and FCS Lab.
 - Winona Heating & Ventilation Co. continued controls programming.
 - WHV held a meeting showing the District how to view and control the new HVAC system.
 - MEP Trades continue rough ins for 6th grade and Area D.
- Ryan Jack Painting continued painting corridors, touching up the FCS Lab, and began touch ups in science.
- VerHalen finished dropping tiles throughout.
- Twin City Tile finished flooring install in the science pod and completed all open punch list items.
- Terrazzo Designs finished terrazzo patching.
- Green Oasis finished landscaping at the front entrance.

Upcoming Week

- Market & Johnson will continue supervising and coordinating trades. M&J will continue installing TV brackets, door hardware, drywall in Area D. Masons will begin setting walls for the Area E addition.
 - Overhead Door will continue installing fire shutters.
 - Cleaners begin in the Science Pod.
 - The District will finish setting up furniture.
 - Epoxy counter top install will begin in the science pod.
 - Area A and FCS Lab punch list on the 21st.
- B&B Electric, Master Metals, and Winona Controls will continue installing devices and finishes in the science pod.
 - Winona Heating & Ventilation Co. will continue controls programming.
 - MEP Trades will continue rough ins for 6th grade and Area D.
 - Winona Controls will install sink fixtures behind the counter install in science.
 - Fire Alarm and Fire Pump test on the 21st.
- Ryan Jack Painting will continue touch ups throughout and will paint the green screen wall in the science pod.
- VerHalen will begin installing acoustic panels in science.
- Esser Glass will finish installing interior glass.

Adding Value to Everything We Do

- Modern Crane will install the exterior stairs from the fire pump room and continue installing the brick ledge in Area A.

Project Manager: Justin Geissler

(715) 225-7885


jgeissler@market-johnson.com


Superintendent: Brian Cutler

(715) 579-0447

bcutler@market-johnson.com

Weekly Photos

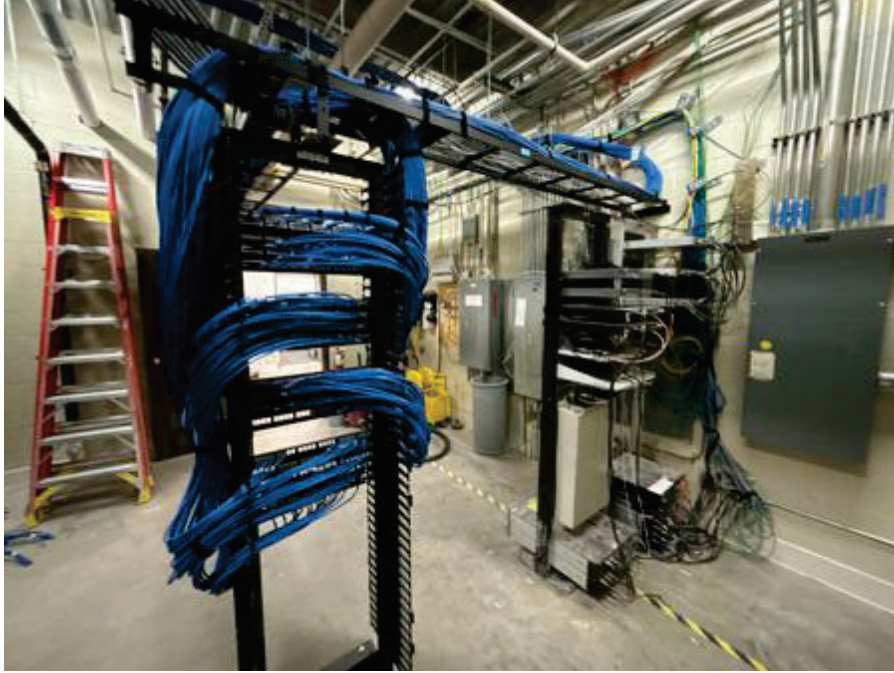

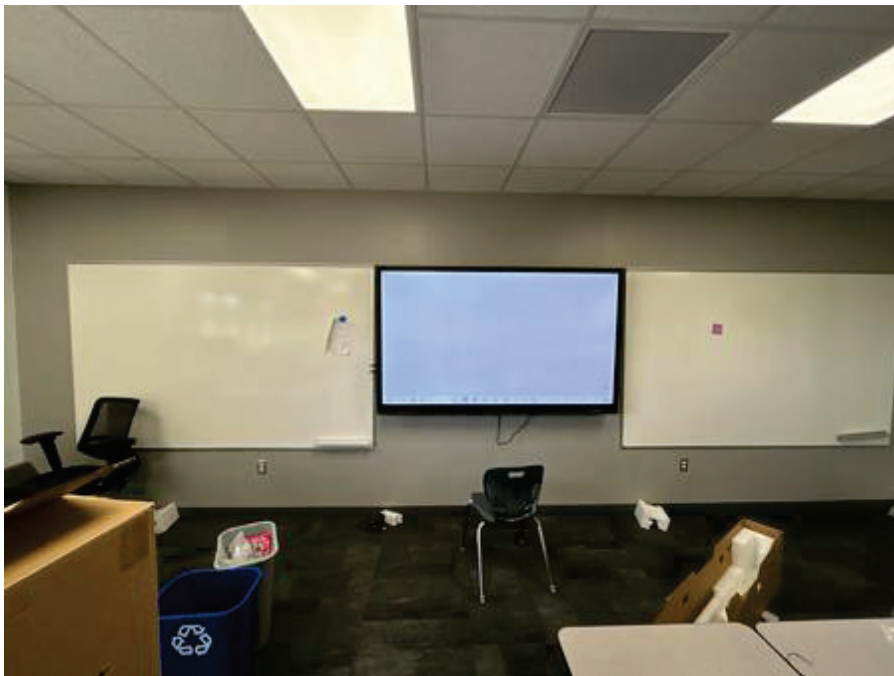



Market & Johnson South Middle School Additions and Alterations

Adding Value to Everything We Do

20

Week of: 8/16/2024



