

# CAPITAL CONSTRUCTION UPDATES 2024-2025

Date: July 7/26/24, 2024

## MEMORIAL TENNIS COURT REPLACEMENT

Complete


## ROOSEVELT WINDOW REPLACEMENT

All the old windows have been removed. The new windows are 80% installed, there was one room that need additional work to prepare the area for windows. That has been completed and windows will be installed later this week. The project is still projected to be completed on time.



## **MONTESSORI CONTROLS**

The contractor has finished pulling all the wire to the control locations. They will begin installation of new device beginning this week. It is anticipated that work will be completed before students arrive.

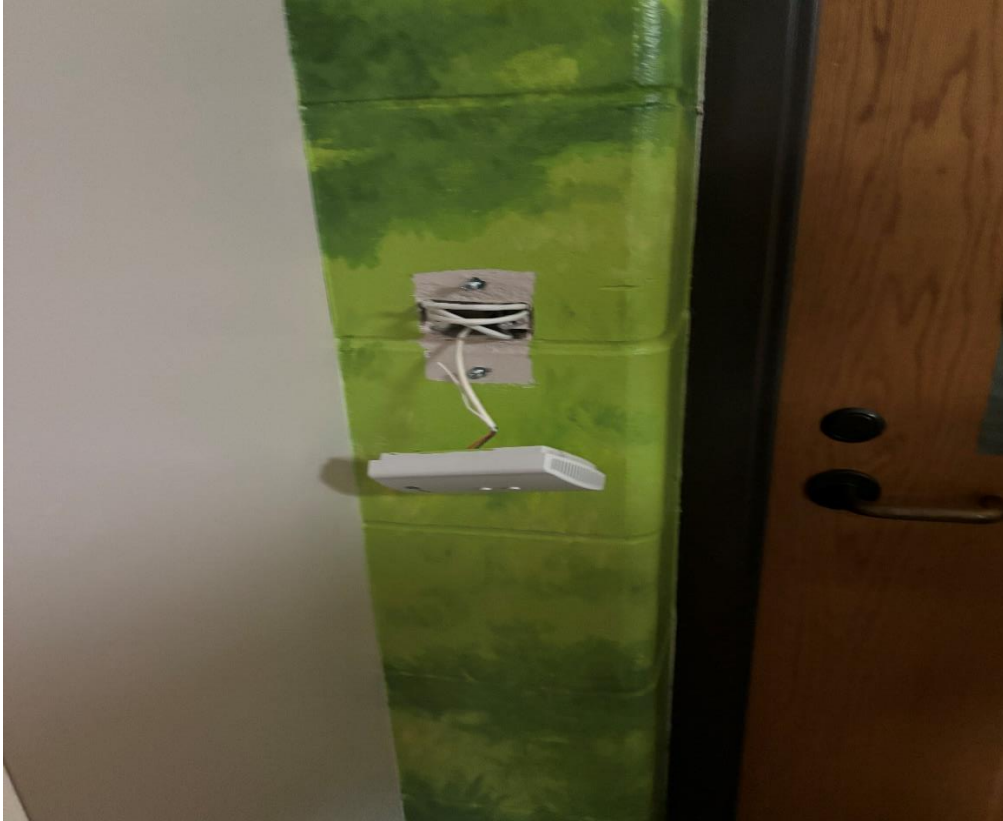

## **NORTH TRACK RESURACING**

The contractor has been delayed because of weather. They anticipate being onsite Wednesday and Thursday to patch, resurface, and line the track.

## **NORTH CHILLER TOWER REPLACEMENT**

The chiller tower replacement will be done early October after the cooling season is complete.

## **ROBBINS GENERATOR WALL REPLACEMENT**

Quotes are being received for the repair work on the wall. They should all be received by the middle of August.

## **SOUTH FREEZER REPLACEMENT**

Work is complete, the food service department will be installing shelving in the next few weeks.

## **SOUTH DISHWASHER REPLACEMENT**

The contractor has completed installing the new wall, new grease trap, and piping. The finish work of the drywall and tiling of the area will be completed this week. The new unit is scheduled to be installed the end of next week.

